MONTHLY DISPATCH • OCTOBER 2026

Official Doc N° 04/2026 • Cabo Frio - RJ

An Altar Raised in Unamar: *Legal Milestone, Works & Spiritual Awakening*

Monthly ministry dispatch covering the formal lease signing for the RCCG Unamar headquarters, electrical and structural upgrades, and early community fruit in Tamoios preparing for the Inaugural Service.

FIELD MISSIONARY
Pr. Thiago Vitalino

SANCTUARY ADDRESS
Rod. Amaral Peixoto (Loja 03)

INAUGURATION TARGET
1st Fortnight of November / 2026

LEGAL STATUS
Lease Signed & Shielded

MISSION CHRONOLOGY • JULY TO NOVEMBER / 2026

Chronological Timeline of Activities in Unamar

A factual chronicle of strategic milestones, field due diligence, leadership approvals, and legal achievements establishing the new RCCG sanctuary.

01

JULY / AUGUST 2026 — INITIAL SURVEY

Territorial Prospecting & 1st Quotation

Field reconnaissance across Tamoios District (Unamar). Initial survey of commercial space on Rua do Tatu (R$ 850/mo) and presentation to leadership for preliminary budgetary review.

02

SEPTEMBER / EARLY OCTOBER 2026 — FIELD EXPEDITION

Market Dynamics & Secondary Survey

Fast-moving commercial leasing turnover in the region rendered the initial property unavailable. Under Pr. Márcio Peres' direct guidance, an immediate survey of 4 local brokerages commenced.

03

OCTOBER 10, 2026 — TECHNICAL DOSSIER

Highway Sanctuary Selection (Store 03)

Issuance of Technical Prospecting Dossier #03/2026. Selection of prime venue directly facing the Emergency Care Unit (~65 m² usable, glass facade, covered porch), with rent negotiated down from R$ 2,000 to R$ 1,600/mo.

04

OCTOBER 29, 2026 — LEGAL MILESTONE

Clicksign Execution & Asset Shielding

Official execution of commercial lease via Clicksign signed by President Pastor Oluwafemi Sunday Israel on behalf of RCCG Brazil, guaranteeing corporate shield and legal security.

05

LATE OCTOBER 2026 — IN PROGRESS

Sanctuary Upgrades, Power Grid & Outreach

Utility connection with ENEL, interior painting, drywall repairs, procurement quotes for 50 chairs and sound equipment, alongside evangelistic family visits in the neighborhood.

06

1ST FORTNIGHT OF NOVEMBER 2026

STRATEGIC TARGET

Sanctuary Dedication & Inaugural Service

Completion of facility renovations, exterior signage installation, seating setup, and hosting the Inaugural Service dedicated to the Lord alongside regional leadership.

CHAPTER 01 • INSTITUTIONAL PROTECTION

Sanctuary Acquisition & Legal Shielding

With deep gratitude to the Lord and in full alignment with the leadership of The Redeemed Christian Church of God (RCCG), on October 29, 2026, we finalized the official lease for the new RCCG sanctuary in Unamar. Strategically located on Av. Independência (flanking Amaral Peixoto Highway), Store 03, directly facing the Tamoios Emergency Unit, this location offers exceptional visibility and easy access for the entire community.

Clicksign Digital Authentication

Official document #03a49fd0-91d4-4aee-a973-652606841b2d, electronically executed with full legal enforceability and permanently archived.

Asset Shielding for Missionary

Clause 11 explicitly protects Pr. Thiago Vitalino's personal CPF from solidary debt liability or historical electric utility (ENEL) arrears.

Full Institutional Representation

Lease executed on behalf of The Redeemed Christian Church of God through President Pastor Oluwafemi Sunday Israel, ensuring institutional perpetuity.

Instrument Facsimile

Executed on 10/29/2026

CLICKSIGN VERIFIED

RAFAEL GROTZ
22 2647-7733
21 96570-1798

CONTRATO PARTICULAR DE LOCAÇÃO DE IMÓVEL PARA FINS RELIGIOSOS

Pelo presente instrumento particular, de um lado, CLÁUDIO DAMIÃO RANGEL RIBEIRO, brasileiro, casado, comerciante, portador do RG nº 42.717 S134 MTPS/RJ e inscrito no CPF sob o nº 094.152.577-50, doravante denominado **LOCADOR.**

LOCATÁRIA – PESSOA JURÍDICA: IGREJA CRISTÃ REDIMIDA DE DEUS, anteriormente denominada IGREJA DE DEUS DOS CRISTÃOS REDIMIDOS, pessoa jurídica de direito privado, de natureza religiosa, inscrita no CNPJ sob o nº 07.738.690/0001-20, com sede na Avenida Valdemar Ferreira, nº 04, Butantã, São Paulo/SP, CEP 05501-000, neste ato representada por seu Presidente e Representante Legal, OLUWAFEMI SUNDAY ISRAEL, de nacionalidade nigeriana, portador da Cédula de Identidade de Estrangeiro (RNE) nº V853910-J, classificação permanente, expedida pelo CGPI/DIREX/DPF, inscrito no CPF sob o nº 235.866.478-24, eleito em 22 de julho de 2025, para mandato compreendido entre 22 de julho de 2025 e 21 de julho de 2027, conforme Certidão do 2º Oficial de Registro de Títulos e Documentos e Civil de Pessoa Jurídica da Comarca da Capital de São Paulo, expedida em 28 de outubro de 2025, com poderes de representação da entidade.

RESPONSÁVEL LOCAL AUTORIZADO PARA PROVIDÊNCIAS JUNTO À ENEL: THIAGO VITALINO OLIVEIRA DA SILVA, brasileiro, nascido em 21/09/1982, portador da Carteira de Identidade RG nº 21.055.016-6, expedida pelo DETRAN/RJ, inscrito no CPF sob o nº 108.317.347-28, residente e domiciliado na Rua Yolanda Cardoso, nº 88, Lagoa Macaé, Rio de Janeiro/RJ, CEP 27931-182, indicado pela LOCATÁRIA exclusivamente para solicitar o restabelecimento do fornecimento de energia elétrica e a transferência da titularidade da unidade consumidora para seu nome, não figurando como segundo locatário, fiador ou devedor solidário das obrigações locatícias.

DAS PARTES E DA FINALIDADE CONTRATUAL: As partes acima qualificadas resolvem celebrar o presente CONTRATO PARTICULAR DE LOCAÇÃO DE IMÓVEL PARA FINS NÃO RESIDENCIAIS, destinado ao funcionamento de estabelecimento religioso (igreja), mediante as cláusulas e condições estabelecidas a seguir, observadas as disposições da Lei Federal nº 8.245/1991 (Lei do Inquilinato) e demais normas legais aplicáveis.

CLÁUSULA PRIMEIRA – OBJETO DA LOCAÇÃO

O LOCADOR aluga à LOCATÁRIA o imóvel comercial, medindo aproximadamente 50 (cinquenta) metros quadrados, com banheiro, localizado na Avenida Independência, nº 0, Loja 03, Sambura, Tamoios, Segundo Distrito de Cabo Frio/RJ, CEP 29900-001.

PARÁGRAFO PRIMEIRO – DO FORNECIMENTO DE ÁGUA E ENERGIA ELÉTRICA: O imóvel possui abastecimento de água proveniente de poço artesiano, com bomba periférica instalada. Fica a LOCATÁRIA expressamente ciente de que não é recomendado o uso dessa água para consumo humano, preparo de alimentos ou ingestão direta, sendo sua utilização indicada apenas para banho, limpeza e lavagem do ambiente, desde que observadas as condições sanitárias adequadas, ressalvada eventual comprovação de sua potabilidade.

Quanto à energia elétrica, caberá à LOCATÁRIA providenciar junto à concessionária ENEL o restabelecimento do fornecimento, ficando autorizado o Sr. THIAGO VITALINO OLIVEIRA DA SILVA, CPF nº 108.317.347-28, a solicitar a

Clicksign

Datas e horários em GMT -03:00 Brasilia
Log gerado em 29 de outubro de 2026. Versão v1.53.0.

CLAUDIO X OLUWAFEMI _ THIAGO (1).pdf

Documento número #03a49fd0-91d4-4aee-a973-652606841b2d
Hash do documento original (SHA256): ea45f527ac8ce52604a7bc2c14d87035b6ef573e13bb29d13b50ac41f7a013f6

Assinaturas

THIAGO VITALINO OLIVEIRA DA SILVA
CPF: 108.317.347-28
Assinou em 29 out 2026 às 14:26:21
THIAGO VITALINO OLIVEIRA DA SILVA

OLUWAFEMI SUNDAY ISRAEL
CPF: 235.866.478-24
Assinou como locatário em 29 out 2026 às 15:18:46
OLUWAFEMI SUNDAY ISRAEL

CLÁUDIO DAMIÃO RANGEL RIBEIRO
CPF: 094.152.577-50
Assinou como locador em 29 out 2026 às 20:30:37
CLÁUDIO DAMIÃO RANGEL RIBEIRO

Log

29 out 2026, 14:03:47 Operador com email rafaelgrotzimobiliaria@gmail.com na Conta acab9e0f-d81f-420f-8b6e-12428e92c7f7 criou este documento número 03a49fd0-91d4-4aee-a973-652606841b2d. Data limite para assinatura do documento: 28 de novembro de 2026 (14:03). Finalização automática após a última assinatura: habilitada. Idioma: Português brasileiro.

29 out 2026, 14:20:42 Operador com email rafaelgrotzimobiliaria@gmail.com na Conta acab9e0f-d81f-420f-8b6e-12428e92c7f7 adicionou à Lista de Assinatura: *******6180 para assinar, via WhatsApp.

Pontos de autenticação: Token via WhatsApp; Nome Completo; CPF; Foto de documento oficial; Assinatura manuscrita. Dados informados pelo Operador para validação do signatário: nome completo THIAGO VITALINO OLIVEIRA DA SILVA.

29 out 2026, 14:20:43 Operador com email rafaelgrotzimobiliaria@gmail.com na Conta acab9e0f-d81f-420f-8b6e-12428e92c7f7 adicionou à Lista de Assinatura: *******5244 para assinar como locatário, via WhatsApp.

Pontos de autenticação: Token via WhatsApp; Nome Completo; CPF; Foto de documento oficial; Assinatura manuscrita. Dados informados pelo Operador para validação do signatário: nome completo OLUWAFEMI SUNDAY ISRAEL.

CHAPTER 02 • FIELD OPERATIONS

Site Renovations & Sanctuary Setup

Taking possession immediately triggered a fast-paced renovation roadmap. Far beyond manual labor, every day on site has been an evangelistic opportunity: while inspecting infrastructure and coordinating contractors, we conducted relational evangelism with nearby business owners and residents.

IN PROGRESS

ENEL Power Connection

Filing utility permits for meter activation and circuit breaker load assessment to power sanctuary air conditioning and sound systems.

Lead: Pr. Thiago Vitalino — Fase 1

SCHEDULED

Plaster, Ceiling & Paint

Contracted drywallers and painters scheduled for ceiling repairs, surface finishing, and liturgical interior painting next week.

Starts: Next Week — Fase 2

IN PROGRESS

Visual Identity & Highway Sign

Manufacturing high-visibility exterior signage facing the daily flow of thousands of commuters on Amaral Peixoto Highway.

Design Approved — Fase 3

PROCUREMENT / ACTION

Furnishings & Audio Gear

Procuring sanctuary padded chairs, mixing console, microphones, and instruments for the main altar.

Underway — Fase 4

CHAPTER 03 • SANCTUARY FACILITIES

Tour of the New Mission Property




FACADE & VISIBILITY

Amaral Peixoto Highway Service Road — Store 03, facing UPA




PANORAMIC PORCH

Welcoming foyer with blindex glass enclosure

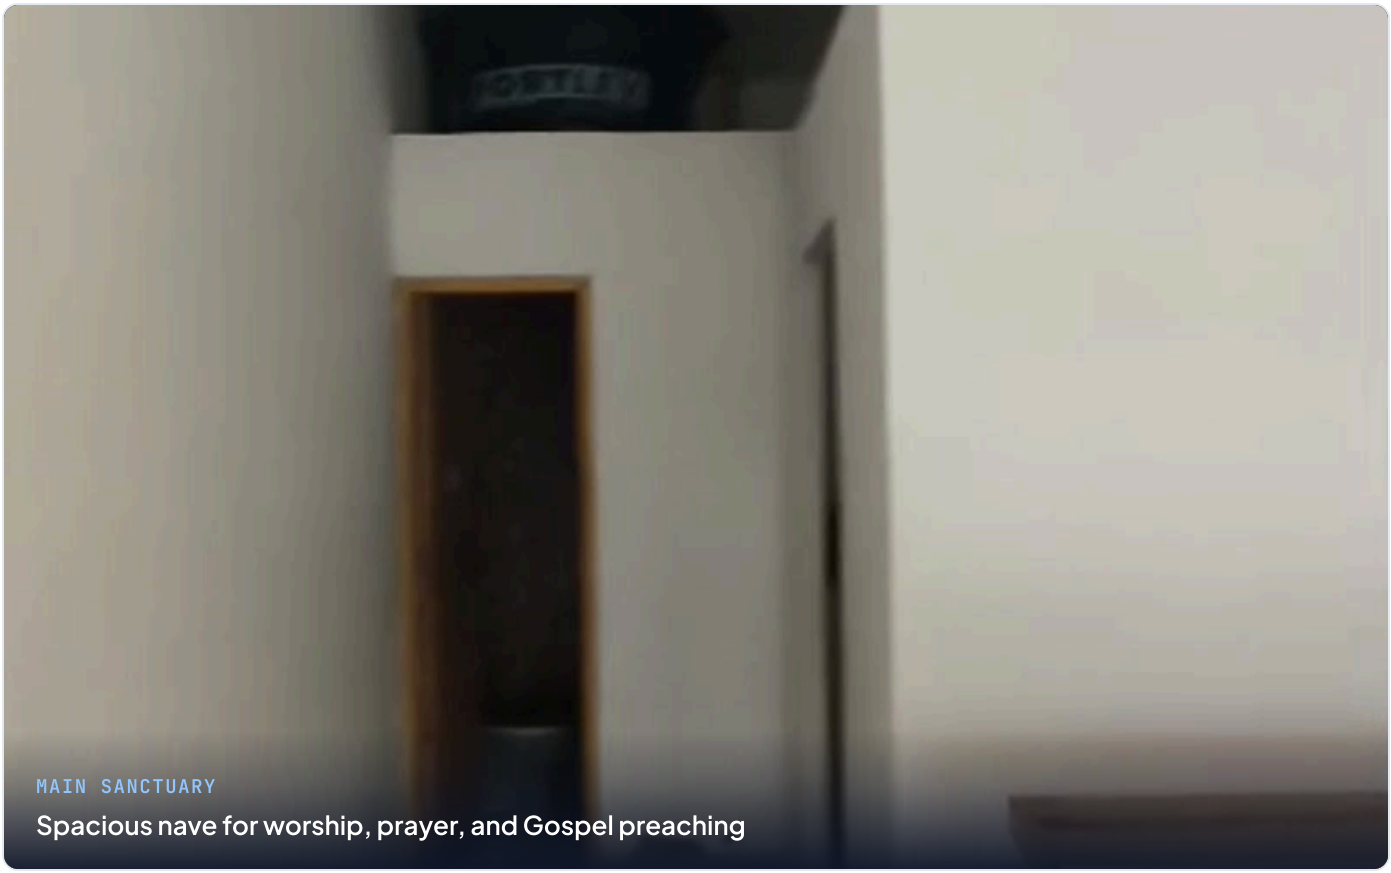

MAIN SANCTUARY

Spacious nave for worship, prayer, and Gospel preaching

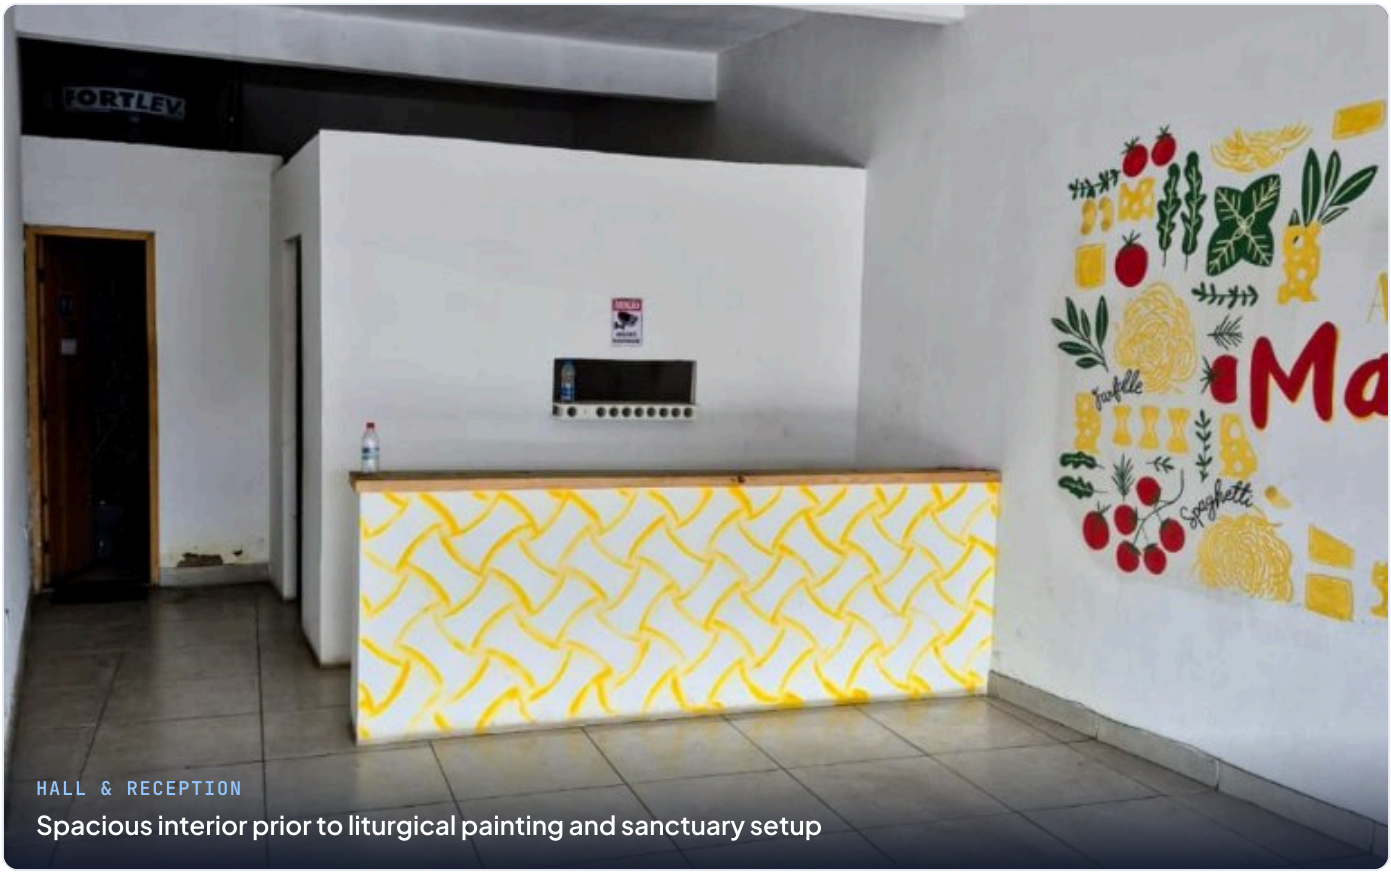


HALL & RECEPTION

Spacious interior prior to liturgical painting and sanctuary setup




INTERIOR INSPECTION

Sanctuary depth offering comfortable capacity for 50+ congregants

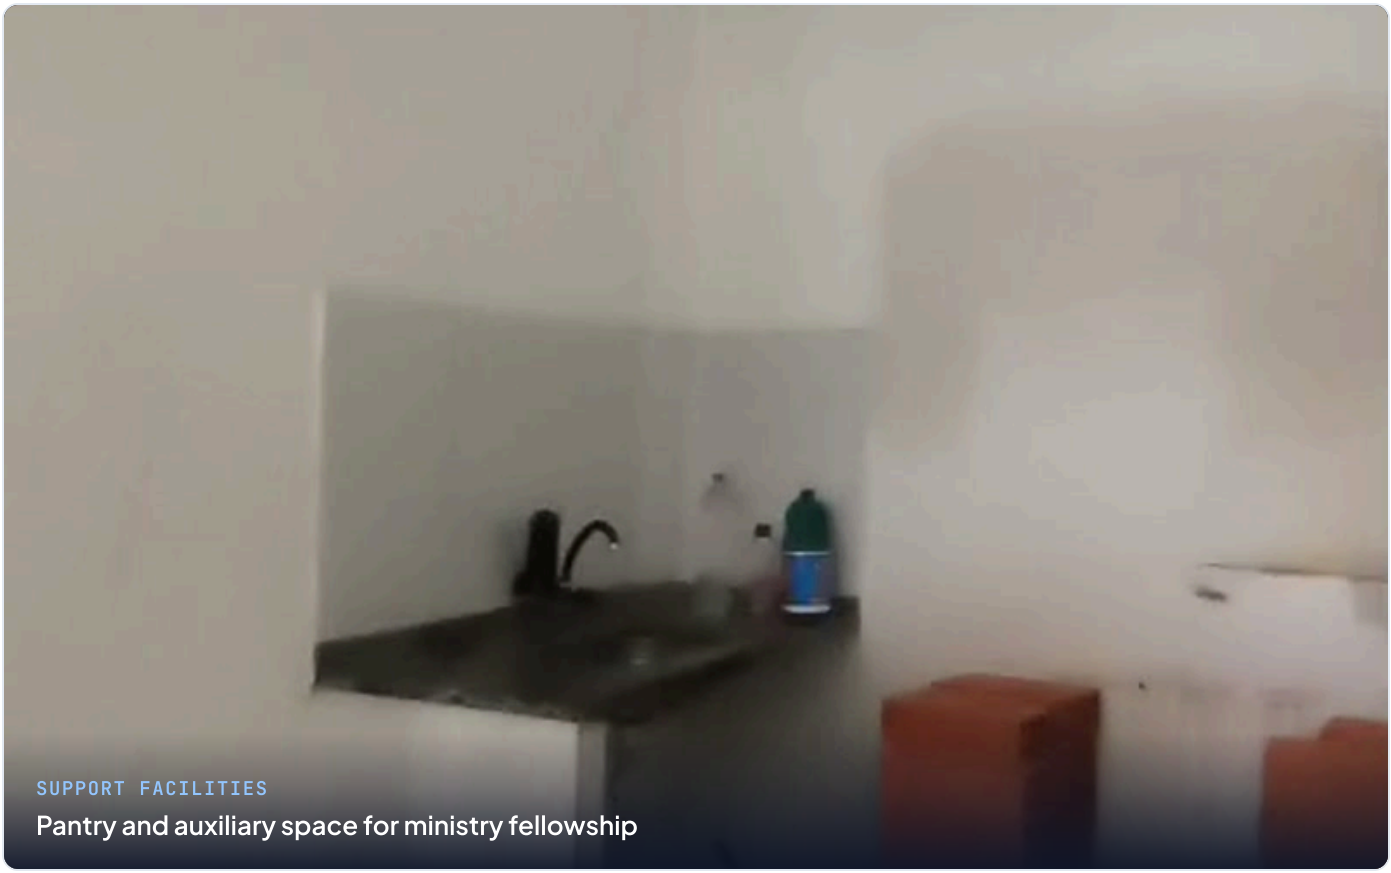

SUPPORT FACILITIES

Pantry and auxiliary space for ministry fellowship

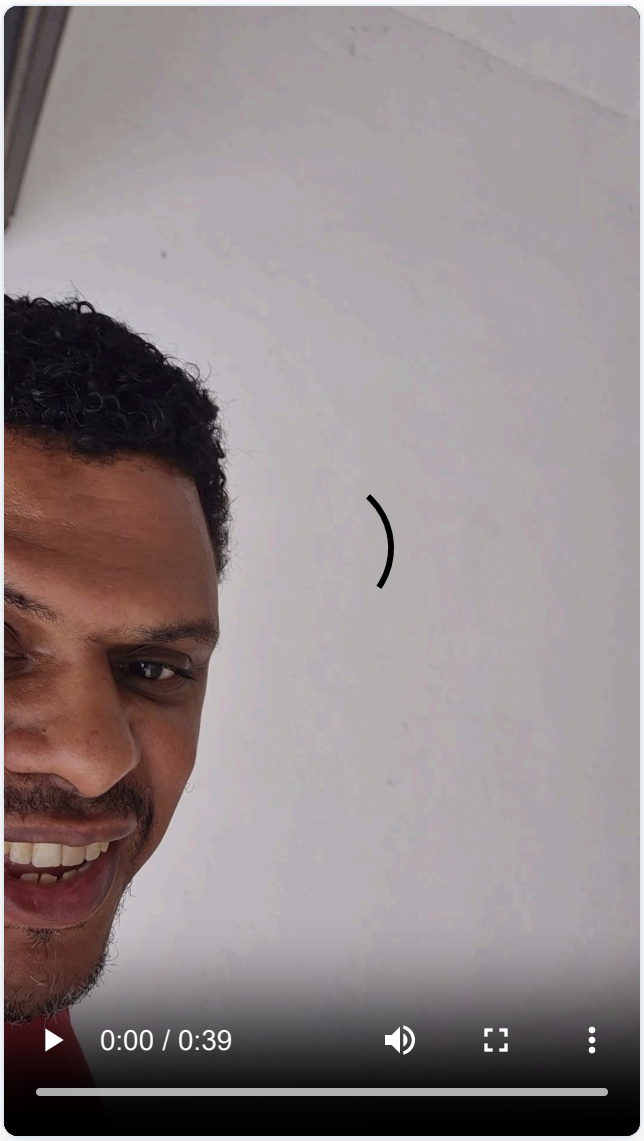

VIDEO WALKTHROUGH

Technical Inspection & Sanctuary Walkthrough

Video recorded on October 14, 2026 during on-site technical inspection with field leadership at the new RCCG Unamar sanctuary.

Open in Google Photos

CHAPTER 04 • SPIRITUAL FRUIT

Gospel in Motion: The Andrade Family

FIELD TESTIMONY • OCTOBER/2026

‘My mother is very eager to visit the church. As soon as it opens, I will bring her with me!’

Even before our doors officially open, Andrade Host's testimony reflects the quiet, powerful work of the Holy Spirit. His mother's heartfelt desire to worship confirms RCCG Unamar's calling as a haven of salvation and family restoration.

Pastoral Conversation: Pr. Thiago Vitalino & Andrade Host


AH
Andrade Host
Parceiro Comercial & Comunidade Local • Unamar
28 DE OUTUBRO DE 2026
Maravilha, Vitalino! Fico muito feliz que vai dar tudo certo e vocês vão assinar e resolver tudo hoje. 🤝 Aproveitando, qual é o nome da sua igreja mesmo? Minha mãe está querendo fazer uma visita lá. Se tiver o Instagram da igreja aí, me manda também para ela dar uma olhada e seguir! 09:42
Que notícia boa! 🙏 Esse é o Instagram da sede (@rccg_ro), visto que ainda estamos por começar em Unamar. Temos o planejamento de abrir até o meio de novembro. Caso sua mãe queira, eu e minha esposa podemos visitá-la! 10:02 ✓✓
30 DE OUTUBRO DE 2026
Boa noite!
Quando vc for inaugurar a igreja me dá um alô, vou levar minha mãe ok 21:42
Boa noite, meu caro! Será uma enorme honra, vou lhe mantendo informado de cada passo. 🙌 21:44 ✓✓

Countdown to the Inaugural Service

Our strategic schedule targets the consecration of the sanctuary for the first fortnight of November 2026. We are coordinating with regional leadership under Pr. Márcio Peres and Pastor Oluwafemi Sunday Israel for a momentous service dedicating this altar.

LITURGICAL TARGET

1st Fortnight • Nov/2026

$ CHAPTER 05 • INTERCESSION COVENANT

Prayer Shield & Faith Targets

We invite every pastor, prayer warrior, and partner to stand with us in these strategic prayer points. Click to seal your prayer commitment:

- [ ] **ENEL Bureaucracy & Power Activation**
  Swift meter inspection and power grid energization without regulatory delay.
- [ ] **Painting, Plaster & Highway Signage**
  Safety for all technicians and craftsmen, and high excellence in finishing.
- [ ] **Sound System & Seating Logistics**
  Flawless delivery and installation of worship instruments and seating.
- [ ] **Neighboring Families Salvation**
  For Andrade Host's mother and households we are visiting across the neighborhood.
- [ ] **Anointing on Inaugural Service**
  That God's presence will fill the temple and many lives will be redeemed.

FIELD MISSIONARY

Pr. Thiago Vitalino

Field Missionary • Missão Salva Vidas

REGIONAL OVERSIGHT

Pr. Márcio Peres

Regional Supervisor • RCCG Brazil

GENERAL LEADERSHIP

Pr. Oluwafemi Sunday Israel

President Pastor • RCCG Brazil

All rights reserved • 2026
